




PRAXION HROS

Project Organization & Stakeholders

Roles, Responsibilities & Module Ownership

April 2026

PROJECT GOVERNANCE STRUCTURE

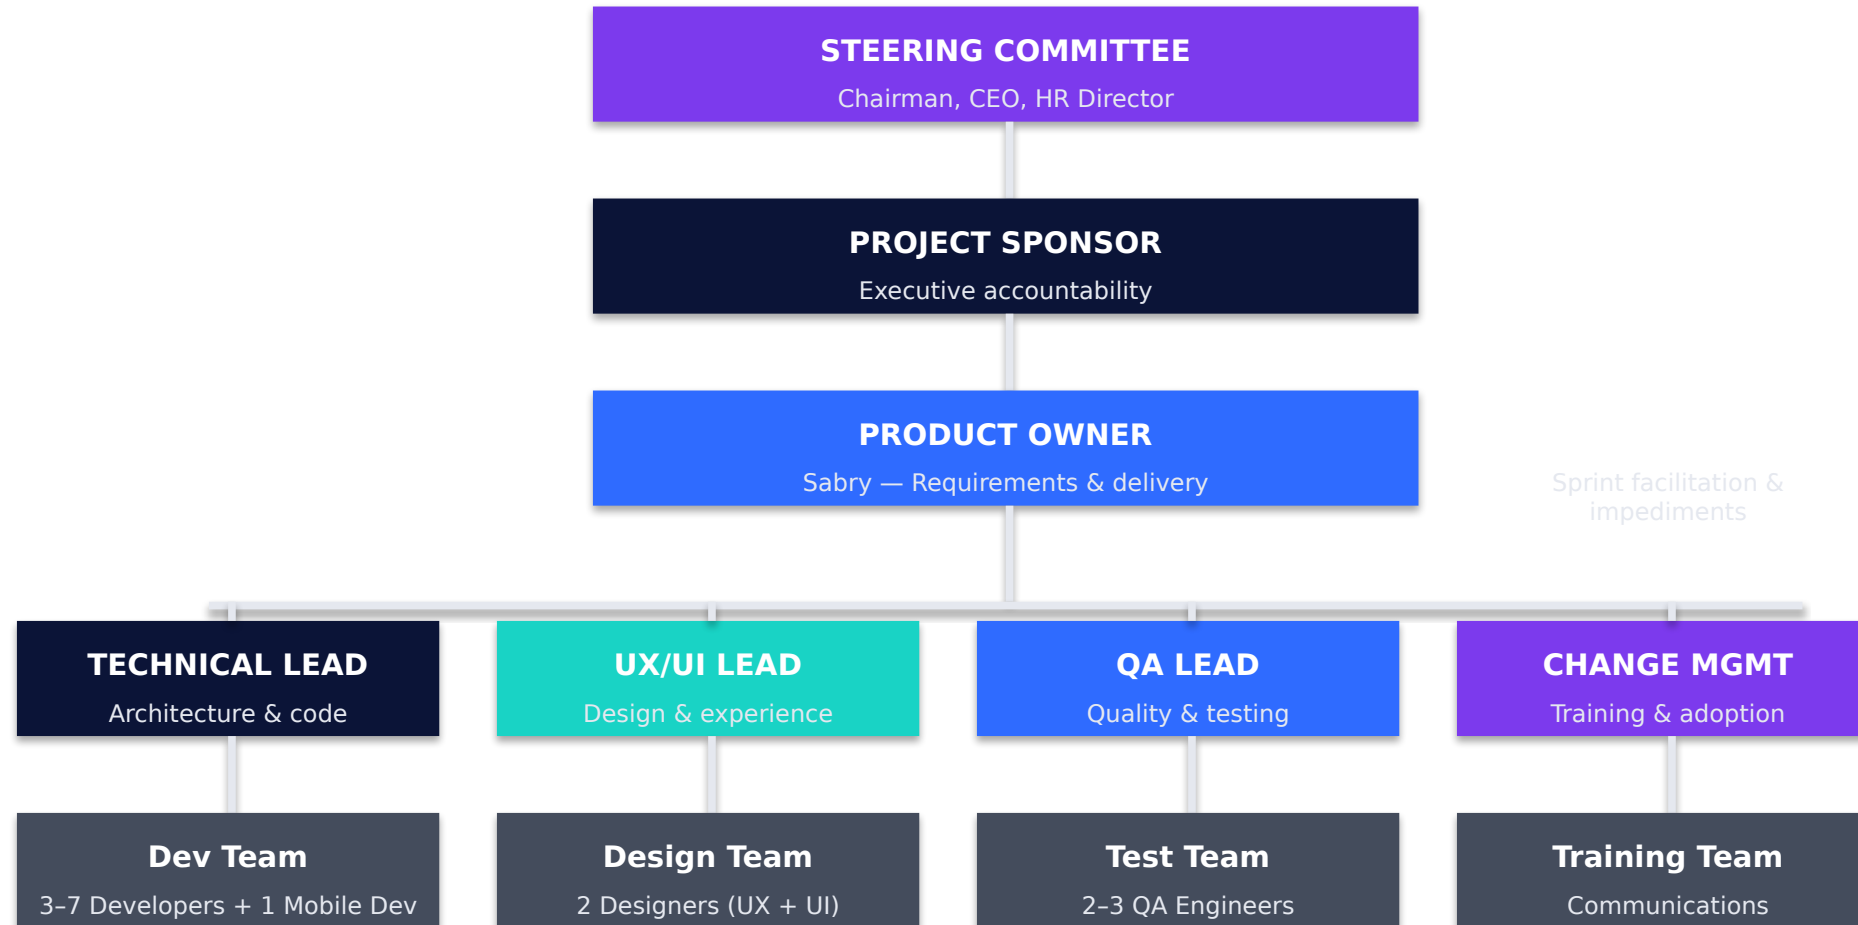

Note: Role-level structure shown. Specific names to be confirmed during Phase 1 kickoff. Team scales from ~5 in Phase 1 to ~10-12 by Phase 3.



CORE PROJECT TEAM ROLES

Product Owner

Defines product vision, prioritizes backlog, writes acceptance criteria, makes scope decisions, represents business stakeholders in sprint ceremonies. Owns the product roadmap.

Technical Lead

Makes architecture decisions, conducts code reviews, mentors developers, ensures technical quality, manages tech debt, and maintains development standards.

UX/UI Lead

Owns the design system, creates wireframes and prototypes, conducts usability testing, ensures WCAG accessibility, and manages the master layout approach.

QA Lead

Defines test strategy, creates test plans and automation, manages bug tracking, conducts regression testing, and gates releases for quality.

Scrum Master

Facilitates sprint ceremonies (planning, standups, reviews, retros), removes impediments, tracks velocity, and coaches the team on agile practices.

Change Management Lead

Develops training materials, manages stakeholder communications, tracks adoption metrics, handles resistance, and ensures smooth organizational transition.



MODULE STAKEHOLDERS — FOUNDATION

MODULES

Module	Primary Stakeholder	Business Owner	Technical Owner	Subject Matter Expert
M1: Core HRIS	HR Director	HR Ops Manager	Technical Lead	HR Specialist
M10: System Admin	IT Director	IT Manager	Technical Lead	Security Officer



MODULE STAKEHOLDERS — PEOPLE MODULES

Module	Primary Stakeholder	Business Owner	Technical Owner	Subject Matter Expert
M2: Recruitment & ATS	HR Director	TA Lead	Technical Lead	Recruiter
M3: Onboarding/Offboarding	HR Director	HR Ops Manager	Technical Lead	HR Specialist
M4: Performance & KPIs	HR Director	L&D Manager	Technical Lead	HR Business Partner
M5: Training & LMS	HR Director	L&D Manager	Technical Lead	Trainer / Facilitator



MODULE STAKEHOLDERS — MONEY

MODULES

Module	Primary Stakeholder	Business Owner	Technical Owner	Subject Matter Expert
M6: Payroll & Compensation	Finance Director	Payroll Manager	Technical Lead	Payroll Specialist
M7: Benefits & Expenses	HR Director	Benefits Admin	Technical Lead	HR Specialist
M8: Contractor Management	Operations Director	Contractor Mgr	Technical Lead	Legal Counsel



MODULE STAKEHOLDERS — INTELLIGENCE & ACCESS

Module	Primary Stakeholder	Business Owner	Technical Owner	Subject Matter Expert
M9: Analytics & Reporting	CEO / COO	Data Analyst	Technical Lead	Business Analyst
M11: Mobile App	HR Director	Product Owner	Mobile Dev Lead	UX Designer
M12: Client Portal	CEO	Client Services Mgr	Technical Lead	Account Manager
M13: Billing & Invoicing	Finance Director	Finance Manager	Technical Lead	Accountant



RACI MATRIX

Responsibility Assignment for Key Decision Areas

R = Responsible (does the work) A = Accountable (final decision) C = Consulted (provides input) I = Informed (kept in the loop)

Decision Area	Steering Committee	Project Sponsor	Product Owner	Technical Lead	UX/UI Lead	QA Lead
Scope Changes / Feature Prioritization	A	C	R	C	I	I
Architecture & Technology Decisions	I	A	C	R	I	I
Budget Allocation & Spend Approval	A	R	C	I	I	I
UI/UX Design & User Experience	I	I	C	I	A	C
Release Go / No-Go Decisions	I	C	A	C	C	R
Sprint Planning & Backlog Priority	I	I	R	C	C	I
Quality Gates & Bug Severity	I	I	C	C	I	R
Vendor & Tool Selection	A	C	C	R	I	I
Data Security & Compliance	A	R	I	R	I	C

COMMUNICATION PLAN



Meeting Cadence and Stakeholder Communication Framework

Meeting	Frequency	Attendees	Purpose	Output
Steering Committee	Monthly	Chairman, CEO, HR Director, Sponsor	Strategic direction, budget review, escalations, phase gates	Decision log, meeting minutes
Sprint Review & Demo	Bi-weekly	Core team, module stakeholders	Demo completed work, collect feedback, validate direction	Sprint report, feedback log
Sprint Planning	Bi-weekly	Product Owner, Tech Lead, Dev team	Define sprint scope, estimate stories, assign tasks	Sprint backlog, commitments
Daily Standup	Daily (15 min)	Dev team, Scrum Master	Progress updates, blockers, coordination	Updated task board
Stakeholder Update	Weekly (email)	All stakeholders, module owners	Status summary, risks, metrics, upcoming milestones	Status report (1-page)
Architecture Review	As needed	Tech Lead, Product Owner, Security Officer	Technical decisions, design reviews, security assessments	Architecture decision records



TEAM FORMATION — NEXT STEPS

Actions to Finalize Project Organization

1

Confirm stakeholder names for each module role position

Fill placeholder roles with actual team members. Ensure each module has an identified Primary Stakeholder, Business Owner, and SME.

Week of Apr 28

2

Schedule Phase 1 kickoff meeting with confirmed team

Bring together the Core HRIS (M1) and System Admin (M10) stakeholders for a detailed requirements walkthrough.

May 5, 2026

3

Set up project communication channels

Create dedicated Slack/Teams channels: #praxion-general, #praxion-dev, #praxion-design. Set up weekly status email distribution list.

May 2026

4

Establish project tracking tools

Set up Jira/Linear for sprint management, Confluence for documentation, Figma for design collaboration.

May 2026

5

Begin Phase 1 sprint planning

Product Owner and Tech Lead collaborate on Sprint 1 backlog. Define first 2-week sprint scope and acceptance criteria.

June 2026
